


Ocean Crest Community Church

Date	Revision	Checked	Approved
25-May-22	Preliminary Schedule		

Activity ID	Activity Name	Original Duration	Start	Finish	2022						2023				
					Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr
Ocean Crest Community Church															
Building Envelope Upgrades															
Key Milestone Dates															
KMD-1000	Project Start	0	18-Jul-22												
KMD-1010	Project Maintenance/ Total Duration	166	18-Jul-22	14-Mar-23											
KMD-1020	Substantial Completion	0		27-Feb-23											
KMD-1030	Project Finish	0		14-Mar-23											
General Requirements															
GNR-1000	Mobilization/Site Facilities	5	18-Jul-22	22-Jul-22											
GNR-1010	Materials & Shop Drawings - Submittals & Approvals	40	18-Jul-22	13-Sep-22											
GNR-1020	Material Procurements & Deliveries	40	16-Aug-22	12-Oct-22											
GNR-1030	Scaffolds & Site Protection	15	25-Jul-22	15-Aug-22											
Construction															
Site Construction															
CNS-1000	Selective Demo	40	16-Aug-22	12-Oct-22											
Rough Carpentry															
CNC-1000	Rough Carpentry	30	14-Sep-22	26-Oct-22											
Roof & Wall Assemblies															
CNR-1001	Roof Assemblies	40	05-Oct-22	01-Dec-22											
CNR-1002	Metal Flashings & Trims	20	10-Nov-22	08-Dec-22											
CNR-1003	Vinyl Soffits	20	18-Nov-22	15-Dec-22											
CNR-1004	Roof & Wall Specialties	15	29-Nov-22	19-Dec-22											
CNW-1000	Exterior Wall Assemblies	40	27-Oct-22	22-Dec-22											
CNW-1010	Exterior Fascia Assemblies	20	02-Dec-22	29-Dec-22											
CNW-1020	Infill Wall Assemblies	15	16-Dec-22	06-Jan-23											
Openings															
CNO-1000	Install Doors & Windows	20	03-Nov-22	01-Dec-22											
Finishes															
CNI-1000	Finishes	20	09-Jan-23	03-Feb-23											
Metals															
CNM-1000	Install Ladders, Guardrails & Handrails	15	23-Jan-23	10-Feb-23											
Electrical															
CNE-1000	Electrical Works & Install Fixtures	30	28-Dec-22	08-Feb-23											
Plumbing															
CNP-1000	Plumbing Works & Install Fixtures	30	28-Dec-22	08-Feb-23											
Close-out															
PS-2000	Deficiencies & Site Clean-up	15	06-Feb-23	27-Feb-23											
PS-3000	Final Deficiencies, Demobilization & Close-out Documents	11	28-Feb-23	14-Mar-23											

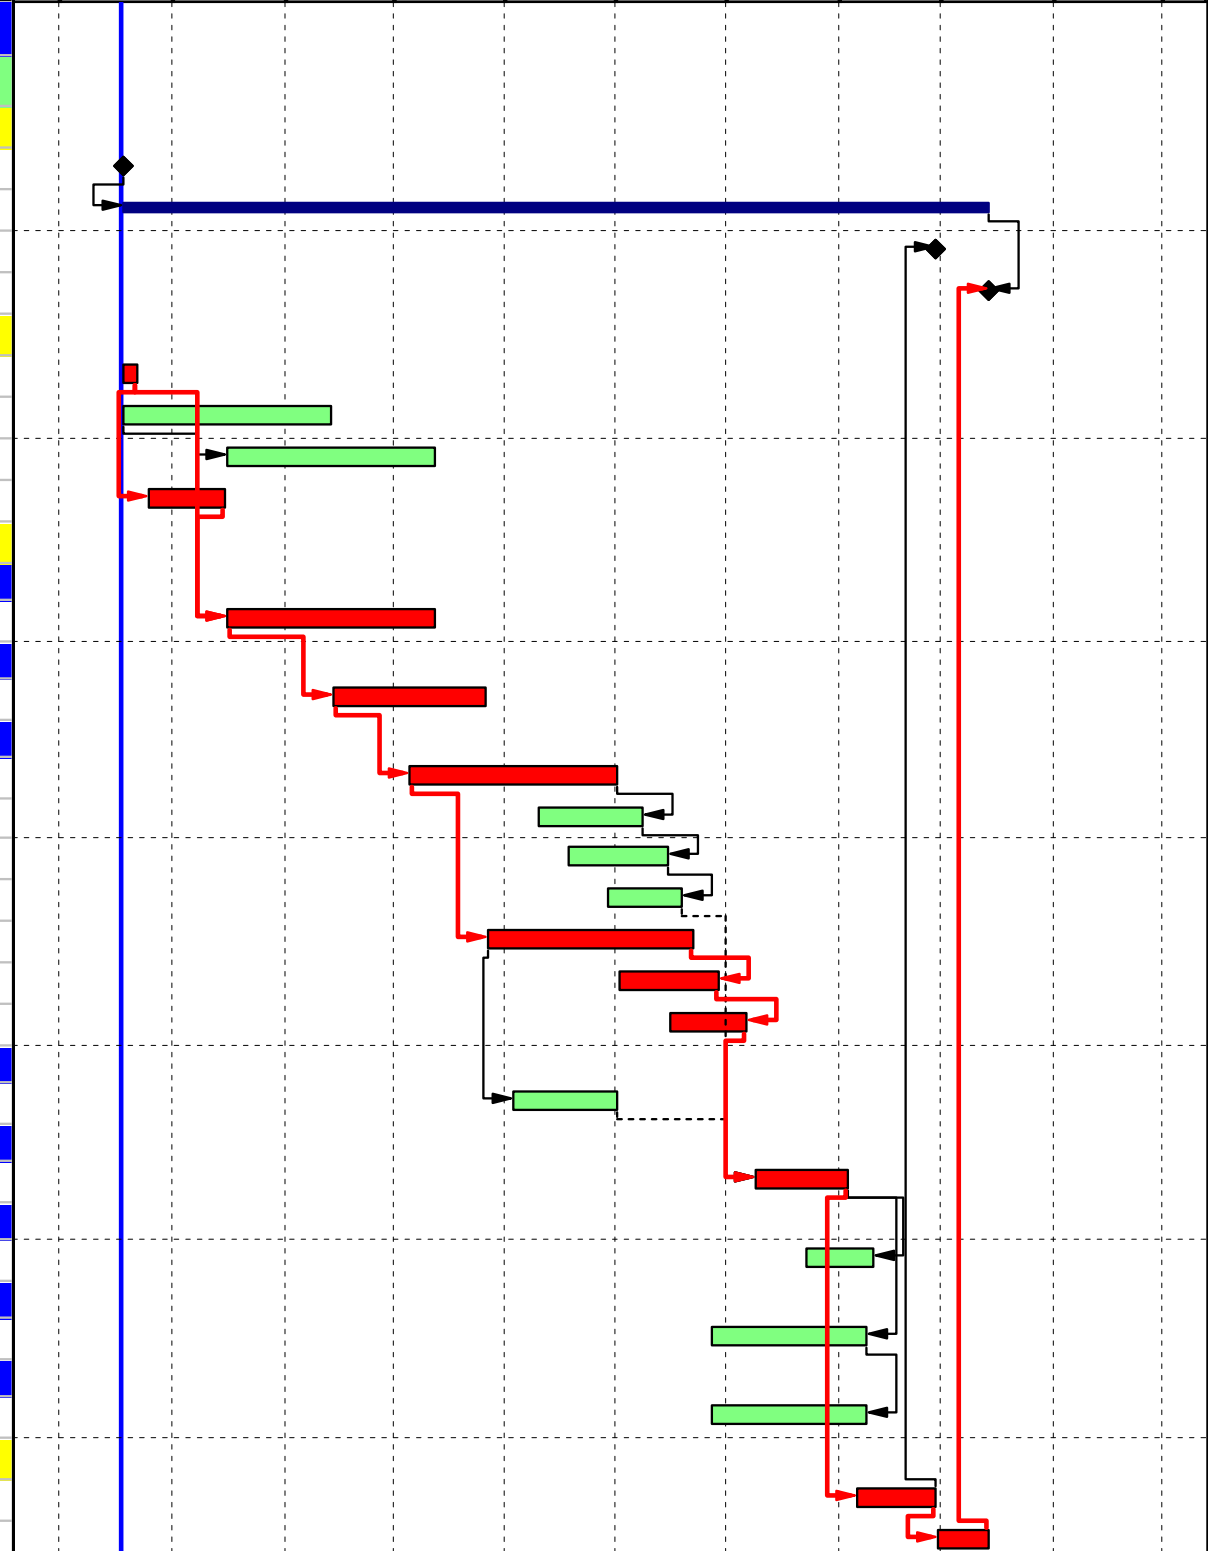

█ Actual Level of Effort █ Critical Remaining Work
█ Actual Work ◆ Milestone
█ Remaining Work
